


4/25/2025
PLOTTED:
OPERATOR: scott.colbert
FILE NAME: \\Egnyteprivate\rette\SharedProjects\11778\117782001\08 CAD\DGN\MPT\117782001_001_MPT_TITLE PAGE.dgn



- STATE HIGHWAY
- TOWNSHIP ROAD
- ... STREAM
- - - MUNICIPAL BOUNDARY
- — DETOUR ROUTE (LENGTH = 13.3 MILES)
- ⬮ — WORK AREA
- (F) — SIGN IDENTIFICATION (SEE SHEET 2)
- — SIGN POST
- — TYPE III BARRICADE
- * — EXTEND TYPE III BARRICADE ACROSS ENTIRE ROADWAY

DETOUR MAP

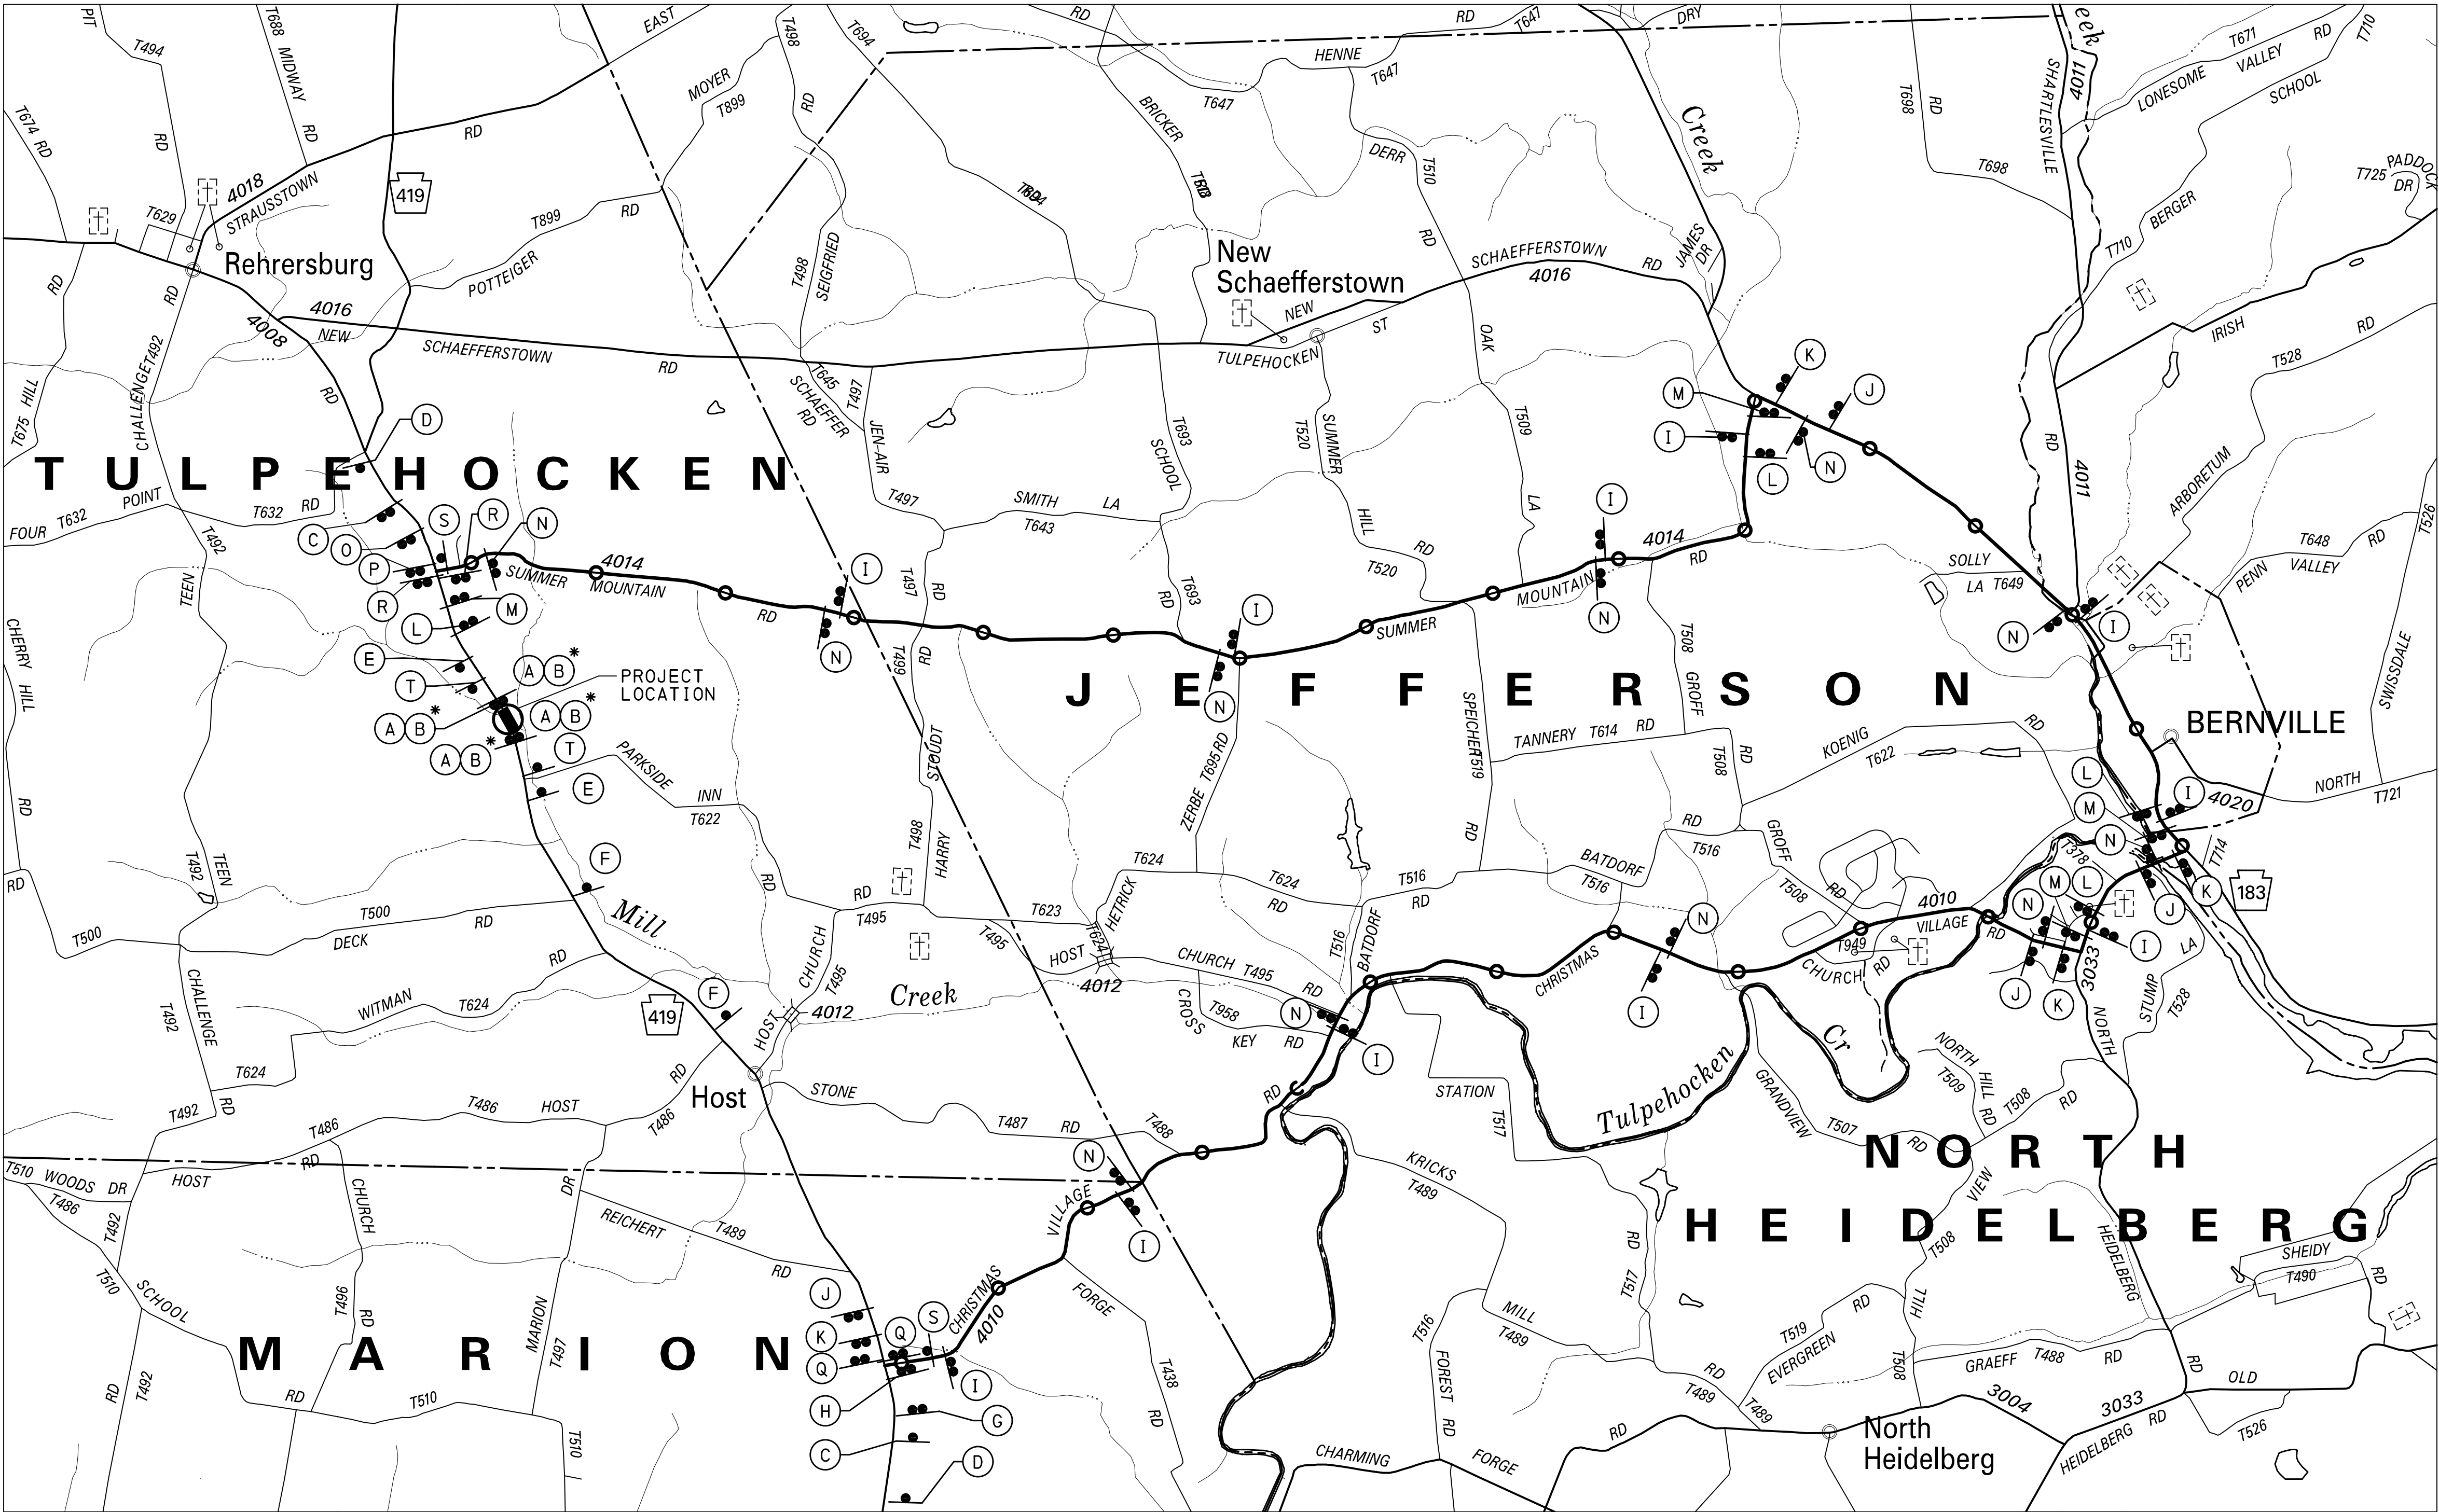

SHEET NUMBER	DESCRIPTION
1	DETOUR MAP & GENERAL NOTES
2	TABULATION SHEET & SEQUENCE OF CONSTRUCTION

TRAFFIC CONTROL PLAN

RECOMMENDED May 1, 20 25

Kerry Cox
DISTRICT TRAFFIC ENGINEER

DISTRICT	COUNTY	ROUTE	SECTION	SHEET
5-0	BERKS	0419	01B	1 OF 2
TULPEHOCKEN TOWNSHIP				
REVISION NUMBER	REVISIONS		DATE	BY

GENERAL NOTES:

THIS WORK CONSISTS OF THE MAINTENANCE OF TRAFFIC AND THE PROTECTION OF THE TRAVELING PUBLIC APPROACHING THE CONSTRUCTION AREA AND WITHIN THE LIMITS OF CONSTRUCTION.

FURNISH, ERECT, PLACE AND MAINTAIN TRAFFIC CONTROL SIGNS AND DEVICES AND MAINTAIN TRAFFIC DURING HOURS OF CONSTRUCTION AND AT ALL OTHER TIMES IN ACCORDANCE WITH THE METHODS INDICATED ON THESE DRAWINGS AND THE FOLLOWING:


1. THE SPECIAL PROVISIONS OF THE CONTRACT.
2. PA CODE, TITLE 67, CHAPTER 212, OFFICIAL TRAFFIC CONTROL DEVICES.
3. PDT PUBLICATION NO. 213, TEMPORARY TRAFFIC CONTROL GUIDELINES.
4. PDT PUBLICATION NO. 35, APPROVE CONSTRUCTION MATERIALS (BULLETIN 15).
5. PDT PUBLICATION NO. 408, SPECIFICATIONS.
6. MANUAL ON UNIFORM TRAFFIC CONTROL DEVICES (MUTCD).

IMMEDIATELY UPON COMPLETION OF THE WORK, REMOVE THE DEVICES. THE DEPARTMENT WILL REMOVE ANY TRAFFIC CONTROL DEVICES ERECTED BY THE DEPARTMENT FORCES.

COVER OR REMOVE ALL SIGNS NOT IN USE.

PLANS PREPARED BY:

RETTEW
RETTEW ASSOCIATES, INC.
3020 COLUMBIA AVE.
LANCASTER, PA 17603



Chad J. Farabaugh

04/25/2025
DATE

DETOUR SIGNING TABULATION INCLUDED IN ITEM NO. 0901-0001 (FOR INFORMATION ONLY)						
PLAN SYMBOL	SIGN	NOMENCLATURE	SIZE	MOUNTING	QUANTITY	REMARKS
(A)		W23-101	96" X 48"	TYPE III BARRICADE	4	PLACE TWO (2) WEEKS PRIOR TO IMPLEMENTING THE DETOUR AND CLOSING THE ROADWAY TO THROUGH TRAFFIC. REMOVE ONCE THE CLOSURE IS IN PLACE.
(B)		R11-2-1	48" X 30"	TYPE III BARRICADE	4	PROVIDE SUFFICIENT NUMBER OF BARRICADES TO COVER ENTIRE ROADWAY. ATTACH YELLOW TYPE B FLASHING WARNING LIGHTS.
(C)		W20-2 W30-1-3	36"X36" 20"X6"	TEMPORARY SIGN POST	2	
(D)		W20-2 W30-1-4	36"X36" 20"X6"	TEMPORARY SIGN POST	2	
(E)		W20-3 W30-1-2	36"X36" 20"X6"	TEMPORARY SIGN POST	2	
(F)		W20-3 W30-1-6	36"X36" 20"X6"	TEMPORARY SIGN POST	2	
(G)		M4-8 M3-1 M1-5 M5-1R	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	1	
(H)		M4-8 M3-1 M1-5 M6-1	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	1	
(I)		M4-8 M3-1 M1-5 M6-3	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	11	
(J)		M4-8 M3-1 M1-5 M5-1L	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	4	
(K)		M4-8 M3-1 M1-5 M6-1	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	4	
(L)		M4-8 M3-3 M1-5 M5-1R	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	4	
(M)		M4-8 M3-3 M1-5 M6-1	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	4	
(N)		M4-8 M3-3 M1-5 M6-3	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	11	
(O)		M4-8 M3-3 M1-5 M5-1L	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	1	
(P)		M4-8 M3-3 M1-5 M6-1	24"X12" 24"X12" 30"X24" 21"X15"	TYPE III BARRICADE	1	
(Q)		R11-3A M4-10R	60"X30" 48"X18"	TYPE III BARRICADE	2	

PLAN SYMBOL	SIGN	NOMENCLATURE	SIZE	MOUNTING	QUANTITY	REMARKS
(R)		R11-3A M4-10L	60"X30" 48"X18"	TYPE III BARRICADE	2	
(S)		M4-8A	24"X18"	TEMPORARY SIGN POST	2	
(T)		W20-3 W30-1-1	36"X36" 20"X6"	TEMPORARY SIGN POST	2	

SUMMARY OF DETOUR SIGNING INCLUDED IN ITEM NO. 0901-0001 (FOR INFORMATION ONLY)			
NOMENCLATURE	DEVICE SIZE OR UNIT	DESCRIPTION	QUANTITY
M1-5	30" X 24"	PENNSYLVANIA ROUTE MARKER	42
M3-1	24" X 12"	NORTH MARKER	21
M3-3	24" X 12"	SOUTH MARKER	21
M4-8	24" X 12"	DETOUR MARKER	42
M4-8A	24" X 18"	END DETOUR	2
M5-1L	21" X 15"	ADVANCE 90 DEG LEFT TURN	5
M5-1R	21" X 15"	ADVANCE 90 DEG RIGHT TURN	4
M6-1	21" X 15"	90 DEG TURN	9
M6-3	21" X 15"	STRAIGHT THROUGH	22
M4-10L	48" X 18"	DETOUR ARROW, LEFT	2
M4-10R	48" X 18"	DETOUR ARROW, RIGHT	2
R11-2-1	48" X 30"	BRIDGE CLOSED	4
R11-3A	60" X 30"	ROAD CLOSED - LOCAL TRAFFIC ONLY	4
W20-2	36" X 36"	ADVANCE DETOUR	4
W20-3	36" X 36"	ROAD CLOSED	4
W23-101	96" X 48"	THIS BRIDGE TO BE CLOSED	4
W30-1-1	20" X 6"	500 FT DISTANCE PANEL	2
W30-1-2	20" X 6"	1000 FT DISTANCE PANEL	2
W30-1-3	20" X 6"	1500 FT DISTANCE PANEL	2
W30-1-4	20" X 6"	1/2 MILE DISTANCE PANEL	2
W30-1-6	20" X 6"	AHEAD DISTANCE PANEL	2
		TYPE III BARRICADES	*
		TEMPORARY SIGN POST	12
		YELLOW TYPE B FLASHING WARNING LIGHTS	*

* PROVIDE SUFFICIENT QUANTITY

TABULATION OF SEPARATE PAY ITEMS			
ITEM NO.	DESCRIPTION	REMARKS	QUANTITY
0901-0240	ADDITIONAL TRAFFIC CONTROL SIGNS		250 SF

DISTRICT	COUNTY	ROUTE	SECTION	SHEET
5-0	BERKS	0419	01B	2 OF 2
TULPEHOCKEN TOWNSHIP				
REVISION NUMBER	REVISIONS			DATE BY

SEQUENCE OF CONSTRUCTION

- ERECT W23-101 SIGNS A MINIMUM OF TWO WEEKS PRIOR TO IMPLEMENTING THE DETOUR AND CLOSING THE ROAD.
- FOR PLACEMENT OF PROTECTIVE FENCE, INSTALLATION OF BMPS, CLEARING AND GRUBBING, AND ANY OTHER ACTIVITY TO BE PERFORMED PRIOR TO IMPLEMENTING THE DETOUR, UTILIZE PATA 101-A, 102, AND 107, WHERE APPROPRIATE.
- ERECT DETOUR SIGNS PER THIS PLAN AND PATA 214 AND IMPLEMENT DETOUR. REMOVE W23-101 SIGNS.
- PROCEED WITH BRIDGE REMOVAL AND CONSTRUCTION PER E&S PLANS, ROADWAY PLANS AND STRUCTURE PLANS.
- BEFORE REOPENING ROAD TO TRAFFIC, REPLACE ALL LANE LINES, CENTERLINES AND EDGE LINES COVERED OR DESTROYED DURING PREVIOUS OPERATIONS.
- REMOVE ALL TRAFFIC CONTROL DEVICES PRIOR TO REOPENING ROAD TO TRAFFIC.
- FOR REMOVAL OF BMPS AND ANY OTHER ACTIVITY TO BE PERFORMED AFTER RE-OPENING SR 0419 TO TRAFFIC, UTILIZE PATA 101-A, 102, AND 107, WHERE APPROPRIATE.

